



Kingsway
Entertainment District



Place des Arts



The Junction

Large Projects Update #17

October 29, 2019

Revised Reporting Approach

- Separate updates for Arena/Event Centre and The Junction.
- Place des Arts reports will now come from the organization as Correspondence to Council.
- Today's report will focus on Arena/Event Centre at the KED.
- The Junction update on November 12.
- Place des Arts update will be attached to November 12 agenda.

Large Projects
Update
#17

October 29, 2019

Kingsway Entertainment District – LPAT and Legal

- Four-day LPAT hearing set for May 5, 2020.
- Waiting for ruling on motion to dismiss Minnow Lake Restoration Group appeal.
- The City has received the application record materials related to Mr. Fortin's proceeding to have the City's by-laws on the KED set aside.
- Service is expected to be imminent.

Large Projects
Update

#17

October 29, 2019

Kingsway Entertainment District

- Project costs to date are approximately 2.2 million or 2.2% of project budget.
- Next report for Arena/Event Centre will be February 4, 2020.

Large Projects
Update

#17

October 29, 2019

Kingsway Entertainment District - Engineering

- Engineering ongoing for:
 - Subdivision streets
 - Storm water management and treatments
 - Kingsway intersection improvements
- Engineering work scheduled for completion in Q2 2020.


Large Projects
Update

#17

October 29, 2019


Large Projects Update #17

October 29, 2019

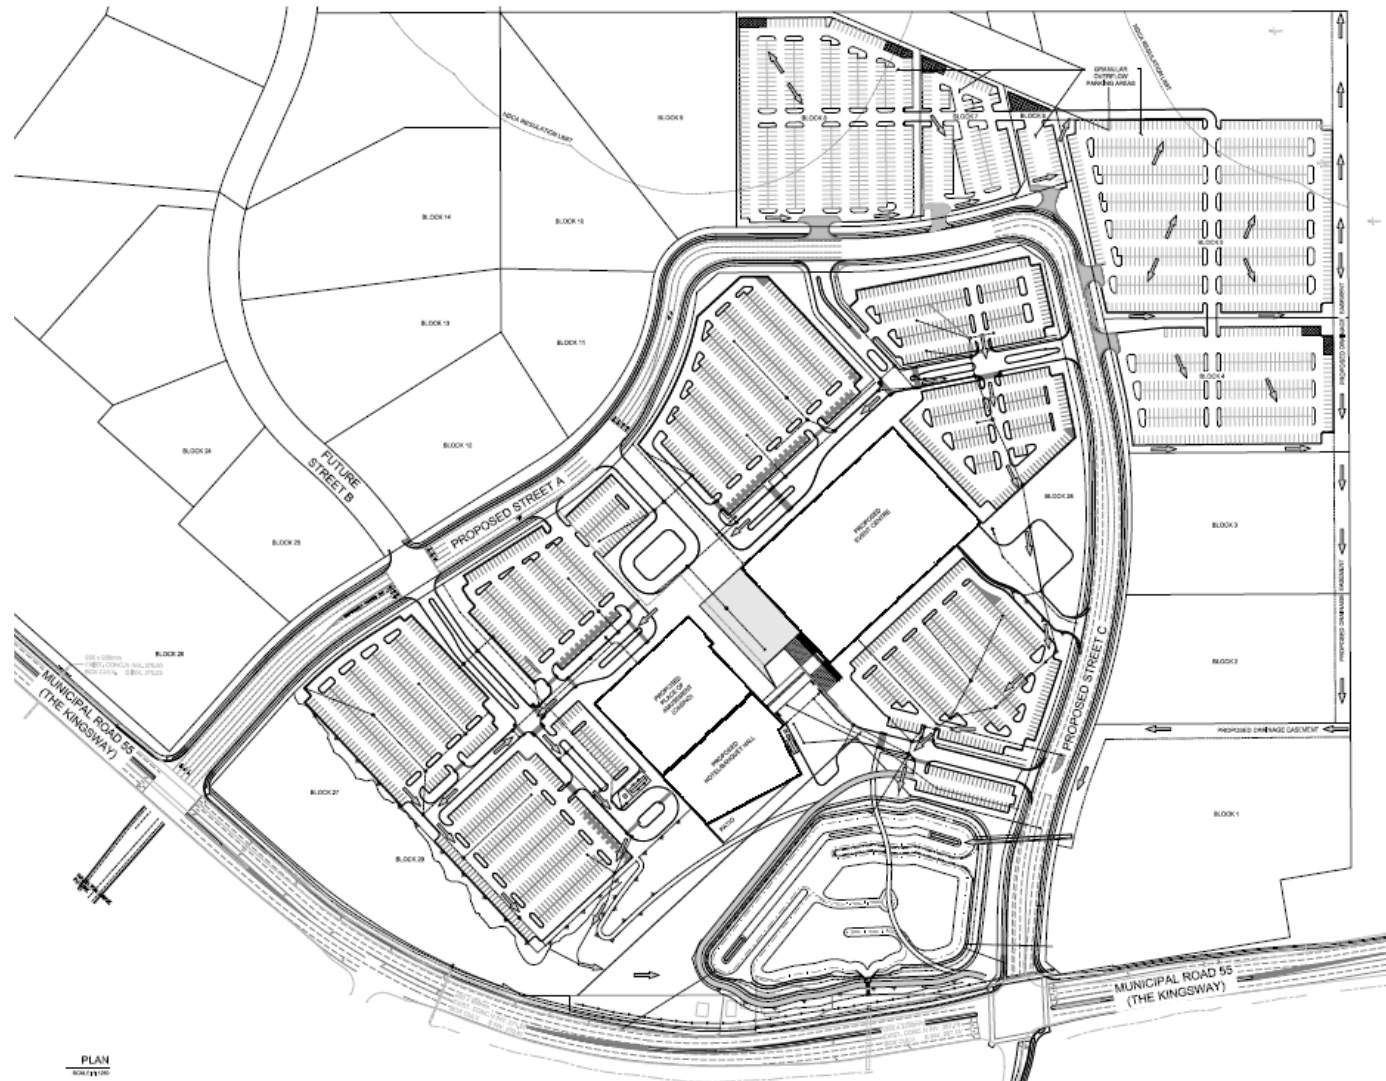


Large Projects Update #17

October 29, 2019

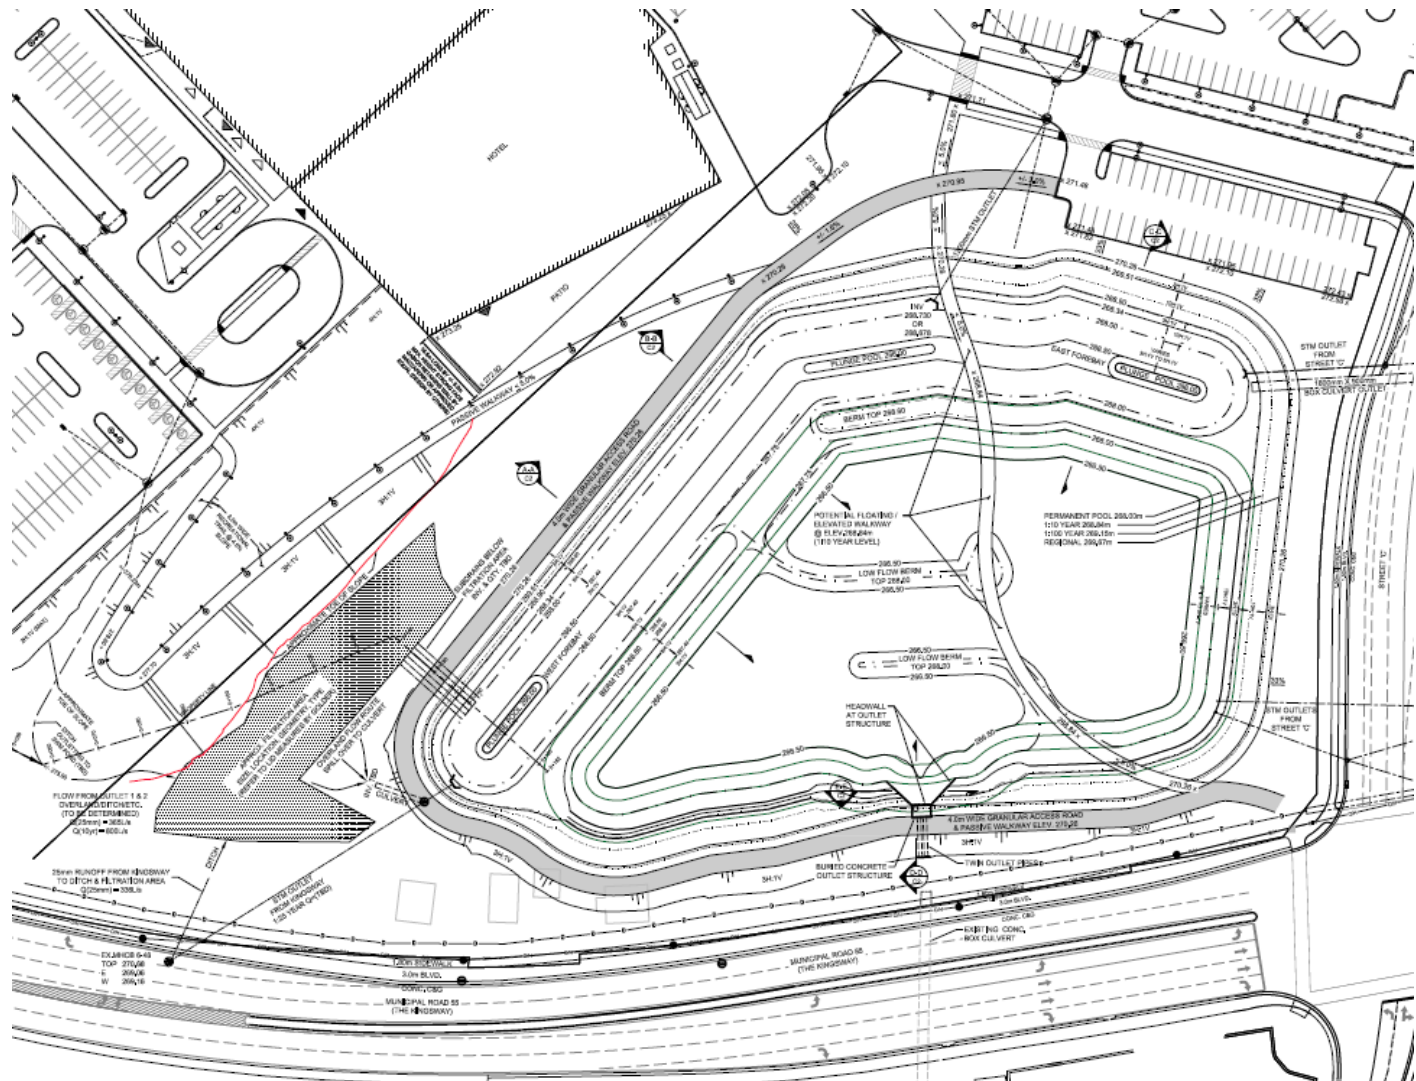

Large Projects Update #17

October 29, 2019

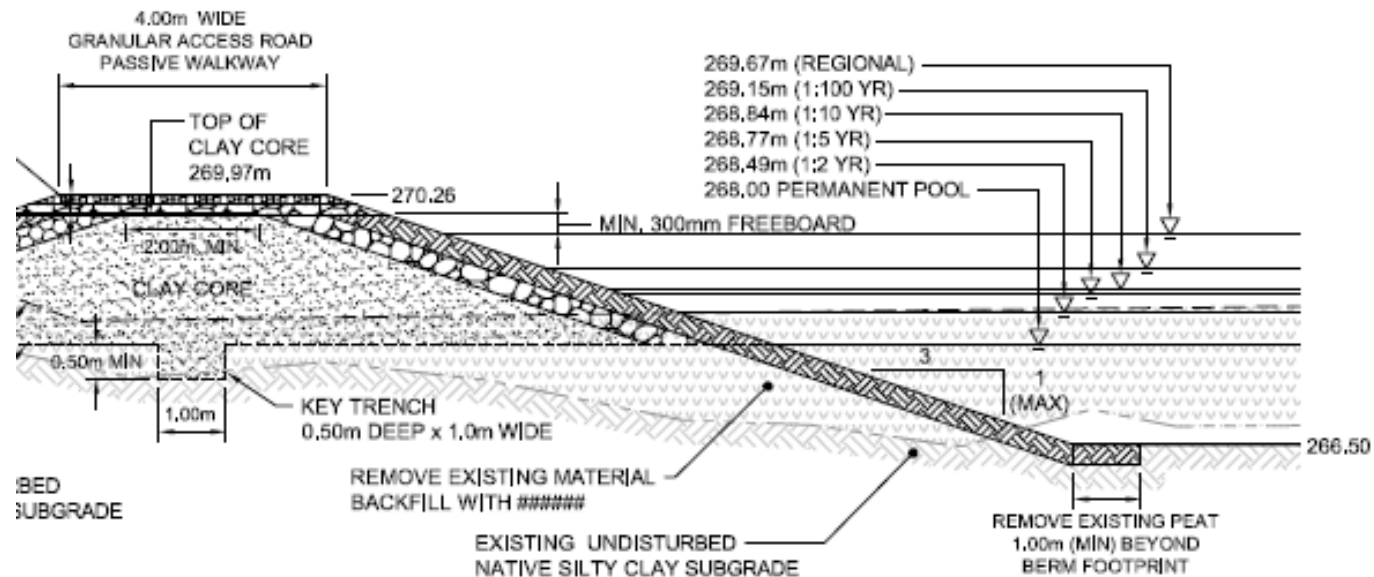

Kingsway Entertainment District

- Questions?

Large Projects
Update
#17

October 29, 2019
